BRUHAT BENGALURU M

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	Improvements to roads and drains of BB Nagara in ward no. 8 kodigehalli
	Consultants	:	Rudraprasad Consultants
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	8-Nov-19
	Project End Date	:	7-Jan-20
	Project Length in Months	:	60 Days

Sl. No	*Assignment*	*Unit*	*Tender Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*	Nov-20
1	Geophysical investigation of site for sinking Borewell for supplying drinking water to the habitation either through the Hand pump, MWS of P.W.S.S by vertical electrical sounding by adopting Venner or Schlumberger's method,	Each	1.00	1.00	100	27-02-21	02-03-21	3	
2	Sinking borewell of 165 mm dia clear using super fast hydraulic rig of capacity 250 PSIG & above CFM & above in all strats including over burden upto 20 mts fixing of casing pipes, collars and cap with necessary cutting, , 0 to 50 m	Rmtr	50.00	50.00	100	27-02-21	02-03-21	3	
3	Sinking borewell of 165 mm dia clear using super fast hydraulic rig of capacity 250 PSIG & above CFM & above in all strats including over burden upto 20 mts fixing of casing pipes, collars and cap with necessary cutting, 50 to 100 m	Rmtr	50.00	50.00	100	27-02-21	02-03-21	3	
4	Sinking borewell of 165 mm dia clear using super fast hydraulic rig of capacity 250 PSIG & above CFM & above in all strats including over burden upto 20 mts fixing of casing pipes, collars and cap with necessary cutting, 100 to 150 m	Rmtr	50.00	50.00	100	27-02-21	02-03-21	3	
5	Sinking borewell of 165 mm dia clear using super fast hydraulic rig of capacity 250 PSIG & above CFM & above in all strats including over burden upto 20 mts fixing of casing pipes, collars and cap with necessary cutting, 150 to 200 m	Rmtr	50.00	50.00	100	27-02-21	02-03-21	3	
6	Sinking borewell of 165 mm dia clear using super fast hydraulic rig of capacity 250 PSIG & above CFM & above in all strats including over burden upto 20 mts fixing of casing pipes, collars and cap with necessary cutting, 200 to 250 m	Rmtr	50.00	50.00	100	27-02-21	02-03-21	3	
7	Sinking borewell of 165 mm dia clear using super fast hydraulic rig of capacity 250 PSIG & above CFM & above in all strats including over burden upto 20 mts fixing of casing pipes, collars and cap with necessary cutting, 250 to 300 m	Rmtr	50.00	50.00	100	27-02-21	02-03-21	3	
8	Sinking borewell of 165 mm dia clear using super fast hydraulic rig of capacity 250 PSIG & above CFM & above in all strats including over burden upto 20 mts fixing of casing pipes, collars and cap with necessary cutting, 300 to 350 m	Rmtr	50.00	50.00	100	27-02-21	02-03-21	3	

J MAHANAGARA PALIKE

alli

20	Dec-20	Jan-21	Feb-21	Mar-21	Apr-21	May-21



RUDRAPRASAD CONSULTANTS
BANGALORE

BRUHAT BENGALURU M

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	Improvements to roads and drains of BB Nagara in ward no. 8 kodigehalli
	Consultants	:	Rudraprasad Consultants
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	8-Nov-19
	Project End Date	:	7-Jan-20
	Project Length in Months	:	60 Days

Sl No	*Assignment*	*Unit*	*Tender Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*	Nov-20
9	Sinking borewell of 165 mm dia clear using super fast hydraulic rig of capacity 250 PSIG & above CFM & above in all strats including over burden upto 20 mts fixing of casing pipes, collars and cap with necessary cutting, 300 to 375 m	Rmtr	25.00	25.00	100	27-02-21	02-03-21	3	
10	Supply of ISI mark 175 mm nominal bore medium black ERW casing pipe of 5 mm thick black electric resistance continuous welded mild steel tube material confirming to IS 1387 / 1993 & manufactured from hot rolled steel skelp / stripes in random length of 4 to 7 mts	Rmtr	54.00	54.00	100	27-02-21	02-03-21	3	
11	Providing and fixing to wall, ceiling and floor unplasticised PVC 6.00 kgs/sqcm working pressure with pipe fittings, wall clips etc., and making good the wall, ceiling and floor for sanitary pipelines including cost of all materials, labour charges, - 250mm dias..	Rmtr	12.00	12.00	100	27-02-21	02-03-21	3	
12	Providing MS Casing pipe collars complete as per specifications and as per the directions of the Engineer-in-charge of the work	Nos	9.00	9.00	100	27-02-21	02-03-21	3	
13	Providing 175mm dia ms casing cap .complete as per specifications and as per the directions of the Engineer-in-charge of the work	Nos	1.00	1.00	100	02-03-21	03-03-21	1	
14	Supply and delivery at site brand New texmo/ innoval/ Lubi/ Sabar / Atalanta/ Calamal/ make suitable for vertical installation in 150mm dia bore well comprising of single stage or multistage CF pump close	Unit	1.00	1.00	100	08-03-21	09-03-21	1	
15	Providing and fixing to wall celling and floor glavanised/ mild steel tubes (medium grade 1.27 kg /mt) B class 50 mm dia nominal bore with all fittings (earth work in trenches to be measured and paid for separately) including cost of all materials,	Rmtr	324.00	324.00	100	08-03-21	09-03-21	1	

J MAHANAGARA PALIKE

alli

0	Dec-20	Jan-21	Feb-21	Mar-21	Apr-21	May-21

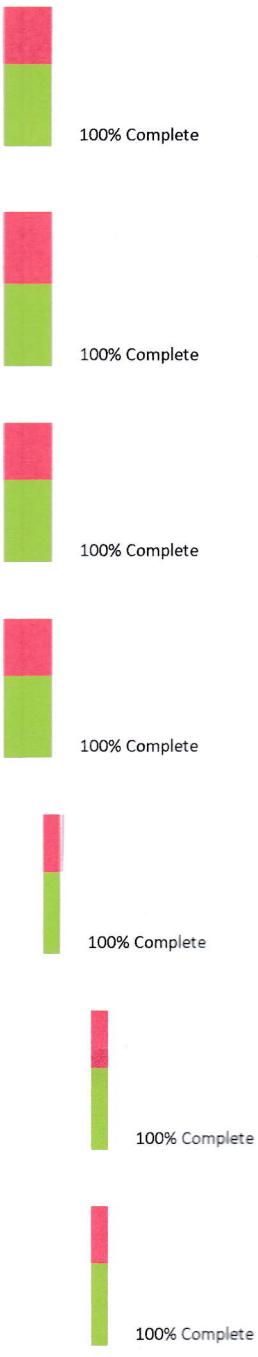

RUDRAPRASAD CONSULTANTS
BANGALORE

BRUHAT BENGALURU M

Clients Name	:	Executive Engineer Byatarayanapura Division	
Project Name	:	Improvements to roads and drains of BB Nagara in ward no. 8 kodigehalli	
Consultants	:	Rudraprasad Consultants	
Project Manager /Team Leader	:	Karthik Rechan	
Project Start Date	:	8-Nov-19	
Project End Date	:	7-Jan-20	
Project Length in Months	:	60 Days	

Sl. No	*Assignment*	*Unit*	*Tender Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*	Nov-20
16	Supplying and drawing 3 core flat PVC sheathed submersible pump cable manufactured with electrolytic grade copper with flexible copper conductor confirming to table 3 class 5 of IS:8130-1984 and virgin grade PVC insulation and Powder coated extrued PVC sheathed suitable for working voltage upto 1100 Volts	Rm	648.00	648.00	100	08-03-21	09-03-21	1	
17	Labour charges for erection of new / repaired submersible pumpset along with gi pipes inculding transportion each length .complete as per specifications and as per the directions of the Engineer-in-charge of the work	Nos	54.00	54.00	100	08-03-21	09-03-21	1	
18	Supplying and flush polished wood board with out front frount plank made of not less than 15mm thick plank after due groove cutting Finishing with necessary on fixing the same to the wall using tapered inverted wooden plugs screws etc.,.	Each	1.00	1.00	100	08-03-21	09-03-21	1	
19	Supplying of 1.1 KV LT UG cable having aluminium condutor PVC insulated shethed, EXTRUDED INNER SHEATHRD galvnised steel,stirp confirming IS 3975;1990 AND extruded PVC outer sheathing armoured cable IS 1554 part 1;1998 and confirming to GTP of group.	Rm	35.00	35.00	100	08-03-21	09-03-21	1	
20	Labour charges for laying of 1.1 K.V class UG cable, P No. 61 / I No. 7.8.1 In existing trencg/duct 6Sqmm to 16 Sqmm) .complete as per specifications and as per the directions of the Engineer-in-charge of the work	Rm	35.00	35.00	100	08-03-21	09-03-21	1	
21	Digging or trenching of 0.6m deep x 0.5 mtr wide refilling the trench to the required ground level and consolidating etc.,.complete as per specifications and as per the directions of the Engineer-in-charge of the work	Rmtr	35.00	35.00	100	08-03-21	09-03-21	1	
22	Supplying and fixing of Class A (meaium duty) GI pipe of wall thickness not less than 3.25mm on pole/wall/drain crossing with necessary clamping arrangements for UG cable of 1.1 KV.	Rmtr	3.00	3.00	100	08-03-21	09-03-21	1	

U MAHANAGARA PALIKE

alli

20	Dec-20	Jan-21	Feb-21	Mar-21	Apr-21	May-21



RUDRAPRASAD CONSULTANTS
BANGALORE

BRUHAT BENGALURU M

	Clients Name	:	Executive Engineer Byatarayanapura Division
	Project Name	:	Improvements to roads and drains of BB Nagara in ward no. 8 kodigehalli
	Consultants	:	Rudraprasad Consultants
	Project Manager /Team Leader	:	Karthik Rechan
	Project Start Date	:	8-Nov-19
	Project End Date	:	7-Jan-20
	Project Length in Months	:	60 Days

Sl. No	*Assignment*	*Unit*	*Tender Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*	Nov-20
23	Supplying and fixing L.T. cast Iron pot head suitable for 1.1 KV class UG cable filled with necessary bituumen/insulating compound complete with terminals, clamps, bolts, nuts and washers etc.,.	No.	1.00	1.00	100	08-03-21	09-03-21	1	
24	Supplying, fixing, wiring, earth electrode for grounding conduits, I.C cutouts and other equipments on the meter board using 40 mm dia 2.90 mm thick GI pipe 2.5 m long buried in a pit. The pit should be filled with equal propotion of solt and charocoal 150 mm alround the pipe to complete depth.	No.	1.00	1.00	100	08-03-21	09-03-21	1	
25	Supplying and fixing of Porcelain fuse channel with cut out on existing wooden / panel using necessary nuts, bolts and washer etc., complete as per specifications and as per the directions of the Engineer-in-charge of the work	Each	3.00	3.00	100	08-03-21	09-03-21	1	
26	Supplying and fixing of heavy duty glands for ug cable 1.1 kv etc., .complete as per specifications and as per the directions of the Engineer-in-charge of the work	Each	6.00	6.00	100	08-03-21	09-03-21	1	
27	Supplying and fixing miniature circuit breakers/solaters on existing MCB distribution boards using necessary fixing materiasl wiring complete as requireds 5 to 32 amps triple pole with all lead and lift, loading,	Each	1.00	1.00	100	08-03-21	09-03-21	1	
28	Fabrication supplying and mounting MS box of 16 SWG suitable for floor /wall mounting, fully weather proof with provision for better heat dissipation, provided with hinged front cover, equipped with tamper proof locking arrangements,	Sqmm	37650.00	37650.00	100	08-03-21	09-03-21	1	
29	Providing and fixing in position 50mm nominal bore gun metal non-return valve horizontal type of approved make including cost of all materials, labour and HOM of equipments with all leads .	Each	1.00	1.00	100	08-03-21	09-03-21	1	
30	Providing NP/CP waste unions conforming to ISI specifications and fixing them in position as per directions including cost of materials, fixtures and conveyance to work spot etc..	No.	2.00	2.00	100	08-03-21	09-03-21	1	

U MAHANAGARA PALIKE

alli

20	Dec-20	Jan-21	Feb-21	Mar-21	Apr-21	May-21

RUDRAPRASAD CONSULTANTS
BANGALORE

BRUHAT BENGALURU M

Clients Name	:	Executive Engineer Byatarayanapura Division	
Project Name	:	Improvements to roads and drains of BB Nagara in ward no. 8 kodigehalli	
Consultants	:	Rudraprasad Consultants	
Project Manager /Team Leader	:	Karthik Rechan	
Project Start Date	:	8-Nov-19	
Project End Date	:	7-Jan-20	
Project Length in Months	:	60 Days	

Sl. No	*Assignment*	*Unit*	*Tender Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*	Nov-20
31	Gate value 50 mm nominal bore gun metal .complete as per specifications and as per the directions of the Engineer-in-charge of the work	No.	3.00	3.00	100	08-03-21	09-03-21	1	
32	Supplying and delivery at site brand new star / Essen/ Lotus/Sun-shines/Adarsh/ GK Controls best indigenous make combined energy meter - cum- control panel board unit of size 600x450 x200 mm minimum mechanically strong vermin and water proof.	No.	1.00	1.00	100	08-03-21	09-03-21	1	
33	Earth work excavation for foundation of buildings, culverts, water supply, sanitary lines and electrical conduits either in pits or in trenches, 1.5m and above in width, in ordinary soil, exceeding 1.5m in depth	cum	33.75	33.75	100	08-03-21	10-03-21	2	
34	Sand Filling in Foundation Trenches as per Drawing & Technical SpecificationMORTH .complete as per specifications and as per the directions of the Engineer-in-charge of the work	cum	5.63	5.63	100	09-03-21	11-03-21	2	
35	Providing and fixing to wall, ceiling and floor high density polyethylene pipes 6.00 kgf/sq.cm working pressure 50mm outside diameter with special flange, compression type fittings, wall clips, making good the wall, ceiling and floor,	Rm	50.00	50.00	100	10-03-21	13-03-21	3	
36	Refilling available earth around pipe lines, cables in layers not exceeding 20cms in depth, compacting each deposited layer by ramming after watering with lead upto 50m. and lift upto 1.5 m. including cost of all labour	cum	28.13	28.13	100	12-03-21	15-03-21	3	
37	Earth work excavation by manual means in Hard soil involving an average horizontal throw upto 2 meters and an average lift upto 0.5m, excavated surface leveled and sides neatly dressed, the disposed earth to be leveled neatly after breaking of clods	Cum	752.53	752.53	100	09-11-20	11-03-21	122	
38	Providing and filling in foundation with granite / trap broken metal 100mm, and downsize and with approved sand including hand packing, ramming, watering, including cost of all materials and labour with all leaed and lift.,,	Cum	76.38	76.38	100	20-11-20	19-03-21	119	

U MAHANAGARA PALIKE

alli

20	Dec-20	Jan-21	Feb-21	Mar-21	Apr-21	May-21

RUDRAPRASAD CONSULTANTS
BANGALORE

BRUHAT BENGALURU M

Clients Name	:	Executive Engineer Byatarayanapura Division	
Project Name	:	Improvements to roads and drains of BB Nagara in ward no. 8 kodigehalli	
Consultants	:	Rudraprasad Consultants	
Project Manager /Team Leader	:	Karthik Rechan	
Project Start Date	:	8-Nov-19	
Project End Date	:	7-Jan-20	
Project Length in Months	:	60 Days	

Sl. No	*Assignment*	*Unit*	*Tender Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
39	Providing and laying in position plain cement concrete of mix M7.5 with OPC cement @ 180 Kgs using 40mm and down size graded granite metal, corse aggregates @ 0.85 cum and fine aggregtes @ 0.58cum machine mixed, concrete laid in layers not exceeding 15 cms thick,	Cum	185.33	185.33	100	12-11-20	22-03-21	130
40	Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for vertical surface such as walls at any thickness, including attached pilasters, buttresses, plinth and string courses cost of all materials, labour	Sqm	953.53	953.53	100	14-11-20	07-04-21	144
41	Providing TMT steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary	Tonne	11.92	11.92	100	13-11-20	02-04-21	140
42	Providing and laying cement concrete using 20mm and down size granite jelly of ready mixed concrete (RMC) for R.C.C works laid in 15cms thick layers and well compacted vibrating, curing, finishing with necessary cement mortar, form works and scaffoldings to withstand pumping of concrete, with all lead and lifts etc., Ready mixed Cement concrete M-20	Cum	193.27	193.27	100	16-11-20	10-04-21	145
43	Providing and Fixing pre cast covering Slab made out of CC 1:2:4 with 10cm thick and Finishing cutting ,including form work,curing,including cost of alll materials, labour,hire charges of machinery,loading,unloading,lead and lift,transportation etc ,	Sqm	388.28	388.28	100	21-11-20	27-04-21	157
44	Providing and laying in position reinforced cement concrete M20 mix with stone aggregates 20mm and downsize for slab (including steel reinforcement) including centering and shuttering, maching mixed, concrete laid in layers not exceeding 15cm	Sqm	43.85	43.85	100	26-04-21	27-04-21	1
46	Providing and laying in position plain cement concrete of mix M20 with OPC cement @ 300 kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.64 cum and fine aggregares @ 0.43 cum with superplastisiser @ 3lts confirming to	Cum	108.95	108.95	100	07-04-21	10-04-21	3

U MAHANAGARA PALIKE

halli

20	Dec-20	Jan-21	Feb-21	Mar-21	Apr-21	May-21

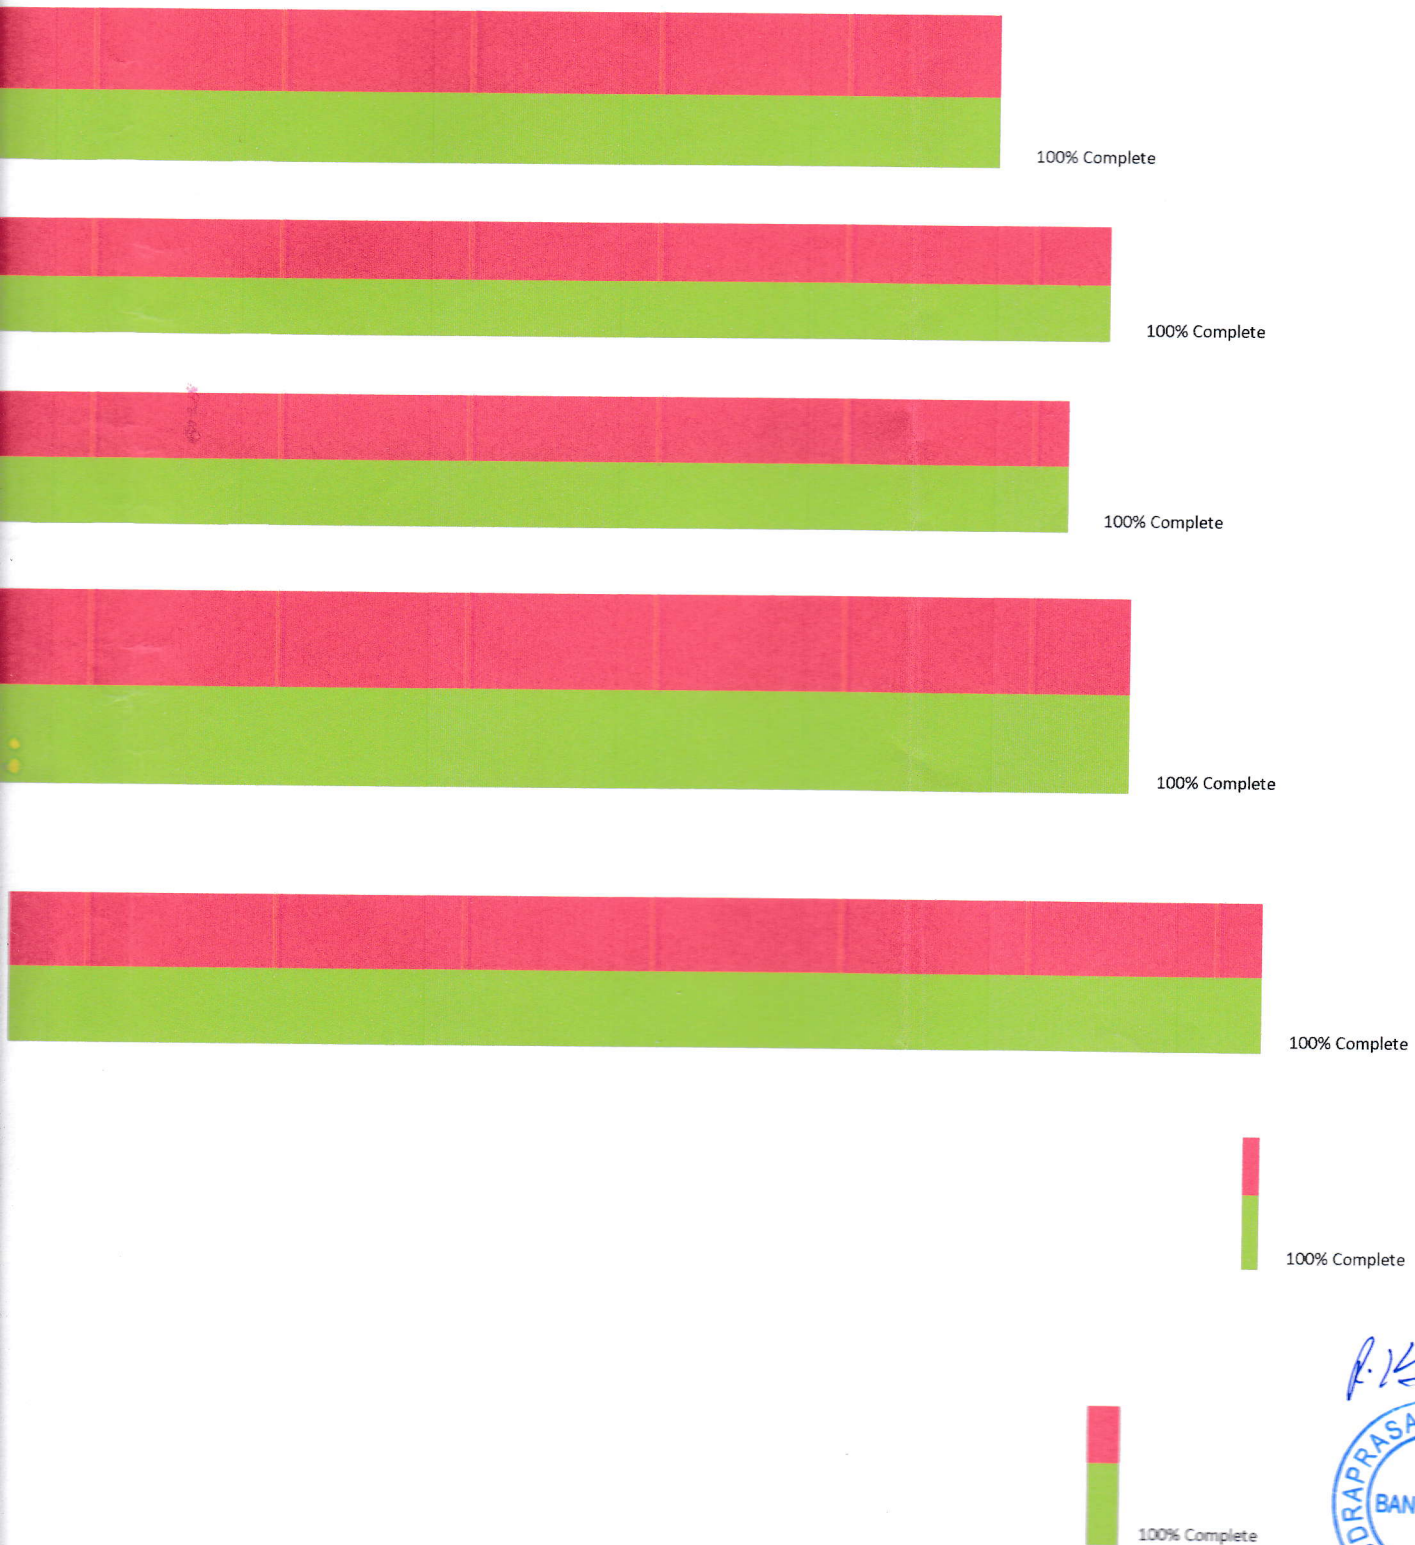

RUDRAPRASAD CONSULTANTS
BANGALORE
